


Book	Owner	Length of Sewer thru Property	Length of R/W thru Property	Number of Manholes
1-159	Strange, P. W.	1,000'	1,000'	5
1-159.1	BRIGGS, Raymond E. & Frances W.	65'	65'	0
1-159.2	CHRISTOPHER, David R. & Edna P.	250'	250'	0
1-159.3	Phillips, E. J. & Frances J.	1,100'	1,100'	5
1-159.4	Strange, P. W.	300'	300'	2
1-159.5	Young, William E. & Mrs. W. E.	150'	150'	0
1-159.6	Phillips, E. J. & Frances J.	150'	150'	0
1-159.7	Henderson, J. B.	50'	50'	0
1-159.8	Henderson, J. B.	200'	220'	1
1-159.9	Childers, W. D.	130'	130'	1
1-159.10	Moser, Robert M. & Kathleen S.	102'	102'	1
1-159.11	Kantorlin, J. B.	102'	102'	1
1-159.12	Young, William E. & Mrs. W. E.	130'	100'	0
1-159.13	Young, Tilda	130'	150'	1
1-159.14	Attaway, A. D.	110'	110'	1
1-159.15	Phillips, E. J. & Frances J.	120'	120'	1
1-159.16	Phillips, E. J. & Frances J.	150'	100'	0
1-159.17	Ansel, J. F.	0'	23'	0
1-159.18	Blakey, William M. & Doris G.	110'	170'	0
1-159.19	Billeshaw, W. F.	300'	170'	0
1-159.20	Williams, W. James	100'	220'	0
1-159.21	Williams, W. James	80'	140'	0
1-159.22	Leslie, W. H.	25'	25'	0
1-159.23	Leslie, W. H.	25'	25'	0
1-159.24	Ansel, J. F.	170'	170'	0
1-159.25	Holland, J. Glenware	210'	210'	0
1-159.26	Williams, Paul H. & Judy K.	150'	150'	0
1-159.27	Shaw, W. E. Inc.	150'	150'	0
1-159.28	Briggs, Ashley C. Jr.	380'	330'	0
1-159.29	Kirchner, Carl E. & Georgia M.	0'	205'	0
1-159.30	Piedmont Land Company	200'	200'	0
1-159.31	Thomson, Madge C.	140'	140'	0
1-159.32	Thomson, Madge C.	140'	140'	0
1-159.33	Tobin, Jackie Marois	40'	130'	0
1-159.34	THOMASON, MADGE C.	130'	130'	0
1-159.35	"	130'	130'	0



- EXPLANATIONS**
- Contractor to put trees to specified lengths.
 - Contractor to place MH flush with ground.
 - Where possible, contractor to save trees that have been flagged.
 - Hold permanent R/W to 10' of center line.
 - Same as P16.1-146.
 - Contractor to place MH flush with ground.
 - Contractor to save as many trees as possible.
 - Contractor to place a "T" connection in line at designated spot.
 - Permanent R/W to be 11' from joint property line.
 - Temporary R/W to be an additional 7'.

- EXPLANATIONS**
- Contractor to put trees to specified lengths.
 - Contractor to place MH flush with ground.
 - Where possible, contractor to save trees that have been flagged.
 - Hold permanent R/W to 10' of center line.
 - Same as P16.1-146.
 - Contractor to place MH flush with ground.
 - Contractor to save as many trees as possible.
 - Contractor to place a "T" connection in line at designated spot.
 - Permanent R/W to be 11' from joint property line.
 - Temporary R/W to be an additional 7'.

- EXPLANATIONS**
- Contractor to be required to build swale ditch at top of cut on West boundary of R/W to channel surface water both towards existing spillway and guarantee to maintain same not to allow any dirt or sediment of any kind to pass into lake.
 - Contractor to place MH flush with ground.
 - All manholes to be left 2' beneath surface of ground.
 - Owner to be allowed to connect to trunk line wherever he selects.

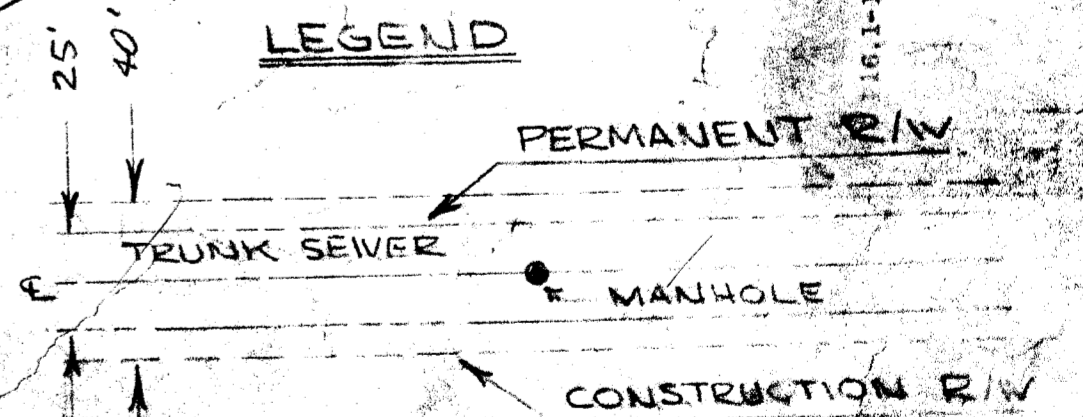

REVISION 04/11/68		
REVISION 10/12/68		
REVISION 10/22/68		
GREENVILLE COUNTY TAX MAPS		
TAX DISTRICT	MAP NUMBER	REVISION
276	P16.1	10-11-68
271		NOV 22 1968
SCALE 1" = 200'		

#1551 Filed This day of July 1967
 And Recorded in Vol. 111 Page 2 of 105 M
 Ollie S. Starnsworth
 Register Mean Conveyance Greenville County, S. C.
